


Bastrop Old Iron Bridge
RAISE Grant
Draft Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	Half 1, 2	
1		Preliminary Schematic Design	22 mons	Mon 8/1/22	Fri 4/5/24																		
2		Environmental Studies and Document	341 days	Mon 8/1/22	Mon 11/20/23																		
3		Resource Studies and Reports	9 mons	Mon 8/1/22	Fri 4/7/23																		
4		Section 106 Coordination	2 mons	Mon 4/10/23	Fri 6/2/23	3																	
5		Section 4(f) De Minimis Coordination	2 mons	Mon 6/5/23	Fri 7/28/23	4																	
6		NEPA Categorical Exclusion	4 mons	Mon 7/31/23	Fri 11/17/23	5																	
7		Environmental Approval	1 day	Mon 11/20/23	Mon 11/20/23	6																	
8		Public Involvement	80 days	Mon 4/10/23	Fri 7/28/23																		
9		Public Meeting	4 mons	Mon 4/10/23	Fri 7/28/23	3																	
10		RAISE Grant Funding Obligation	3 mons	Tue 11/21/23	Mon 2/12/24	7																	
11		PS&E	18 mons	Tue 11/21/23	Mon 4/7/25	7																	
12		Permitting	12 mons	Tue 11/21/23	Mon 10/21/24	7																	
13		Ready to Let	0 days	Mon 4/7/25	Mon 4/7/25	11																	
14		Procurement	6 mons	Tue 4/8/25	Mon 9/22/25	13																	
15		Construction	24 mons	Tue 9/23/25	Mon 7/26/27	14																	

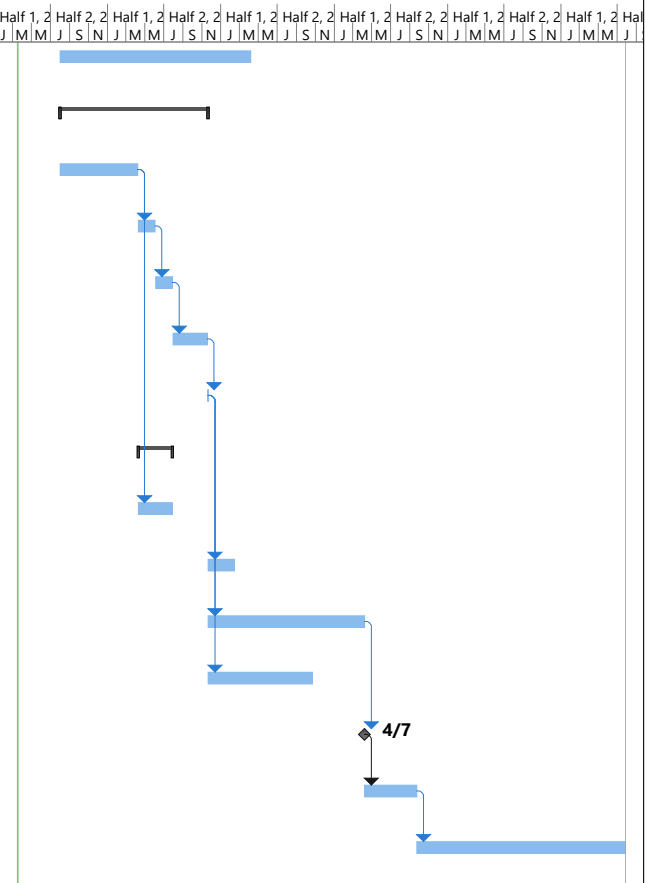

Version Date: Fri 3/18/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
